

OKPSBN Weekly Status Report


Oklahoma Office of Management & Enterprise Services (OMES) - OKPSBN

Status Meeting Agenda

Status on 23 November 2015	Prior Status	Green	Current Status	Green
Green	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.			
Yellow	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.			
Red	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.			
<p>Attendees/Invitees:</p> <ul style="list-style-type: none"> ○ OKPSBN Steering Committee: Ben Gherezgiher, Nikki Cassingham, Juana Riley, David Baisden, Jason Mitchusson, Nick Carrao, Bill Scott, Ralph Suter ○ Televate: David Fein, Rick Burke, Ian Ross, Matthew Plache <p>Agenda:</p> <ul style="list-style-type: none"> ➤ Completed and upcoming tasks ➤ Update for ongoing tasks ➤ Discussion and future tasks 				
November 16th- November 20th Tasks		November 23rd- November 27th Tasks		
Schedule incomplete coverage reviews		Schedule incomplete coverage reviews		
Progress towards 100% survey completion		Progress towards 100% survey completion		
FirstNet Question Follow up		Project Plan- Public Safety Association Registration		
Complete Governance Document		Complete Governance Document		
FN State Plan Evaluation Process – Planning Work Group		FN State Plan Evaluation Process – Planning and Identifying Work Groups		

State of Oklahoma State and Local Implementation Grant Program

Status on 23 November 2015	Prior Status	Green	Current Status	Green
Green	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.			
Yellow	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.			
Red	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.			

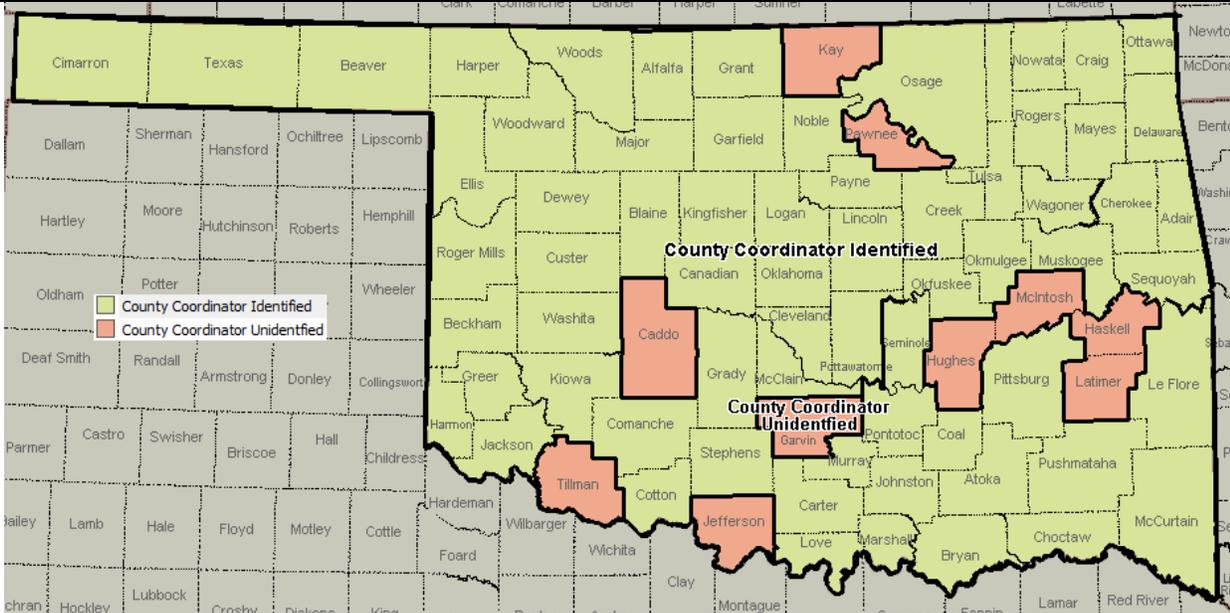

Updated: County Coordinator

This map depicts the Public Safety Entities (PSEs) from each county that have provided a county coordinator contact.

- County coordinator strategy: Emergency Manager, PSAP Manager, then Sheriff
 - County coordinator request emails sent 5/11
 - 67 county coordinators have been identified
 - 11 county coordinators have provided an updated contact list for their county
 - 16 quick start county coordinators identified
 - 4 tribal coordinators have been identified

State of Oklahoma State and Local Implementation Grant Program

Status on 23 November 2015	Prior Status	Green	Current Status	Green	
Green	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.				
Yellow	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.				
Red	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.				
Oklahoma PSBN Project Weekly Status Call Action Item Register					
Action Item	Owner	Date Assigned	Due Date	Priority (H, M, L)	Comments
ODOT Public Works 8 field divisions Personnel/Vehicle Counts	Jason	9/9/2015	9/17/2015	H	As soon as Possible
Statewide Agencies to Include in coverage reviews and userpop	OKPSBN Team	8/3/2015	8/3/2015	H	
Completed Action Items					
LMR coverage GIS files	Nick	6/29/2015	7/13/2015	H	
Homeland Security Regional Coordinators	Ian	8/24/2015	8/27/2015	H	Will Schedule Coverage Reviews
Governance Draft Document	David Fein/ Rick	8/24/2015	8/27/2015	H	Review and Provide OKPSBN
Homeland Security Regional Coordinators	Nikki	8/24/2015	8/27/2015	H	Complete

State of Oklahoma State and Local Implementation Grant Program

Status on 23 November 2015	Prior Status	Green	Current Status	Green	
Green	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.				
Yellow	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.				
Red	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.				
Oklahoma Email Blast	Juana Riley	8/24/2015	8/24/2015	H	Complete
Governance Draft Document	Mathew Plache	8/24/2015	8/27/2015	H	Complete
Critical Infrastructure	Ben G/ Personnel	6/22/2015	7/13/2015	H	
OKC and Tulsa outreach and education meetings letters sent and date set	OKPSBN Team	6/22/2015	7/13/2015	H	Official Dates Set?
Statewide incident data	Ben G/ Personnel	6/22/2015	7/13/2015	H	
<ul style="list-style-type: none"> ○ Invoices and Deliverables <ul style="list-style-type: none"> ○ None at this time ○ Upcoming Events, Travel, New Business: <ul style="list-style-type: none"> ○ 					
