

# OKPSBN Weekly Status Report

Oklahoma Office of Management & Enterprise Services (OMES) - OKPSBN

## Status Meeting Agenda


<b>Status on 21 March 2016</b>	<b>Prior Status</b>	<b>Green</b>	<b>Current Status</b>	<b>Green</b>
<b>Green</b>	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.			
<b>Yellow</b>	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.			
<b>Red</b>	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.			
<p><b>Attendees/Invitees:</b></p> <ul style="list-style-type: none"> <li>○ OKPSBN Steering Committee: Ben Gherezgiher, Nikki Cassingham, Juana Riley, David Baisden, Nick Carrao, Bill Scott, Ralph Suter</li> <li>○ Televate: David Fein, Rick Burke, Ian Ross, Matthew Plache</li> </ul> <p><b>Agenda:</b></p> <ul style="list-style-type: none"> <li>➤ <b>Matthew Status</b></li> <li>➤ <b>State Plan Process Working Group</b></li> <li>➤ <b>Update for ongoing tasks</b></li> <li>➤ <b>Discussion and future tasks</b></li> </ul>				
<b>March 7<sup>th</sup> - March 21<sup>st</sup> Tasks</b>		<b>March 21<sup>st</sup> – April 4<sup>th</sup> Tasks</b>		
Website Update		Continuing Website Update		
Schedule incomplete coverage reviews		Schedule incomplete coverage reviews		
Progress towards 100% survey completion/ UserPOP Email Blast Prep		Progress towards 100% survey completion/ UserPOP Email Blast Prep		
Governance Interviews		Governance Interviews		
Tribal Coordination for multi tribe in person meeting		Outreach and Education Invitations		

State of Oklahoma State and Local Implementation Grant Program


<b>Status on 21 March 2016</b>	<b>Prior Status</b>	<b>Green</b>	<b>Current Status</b>	<b>Green</b>
--------------------------------	---------------------	--------------	-----------------------	--------------

<b>Green</b>	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.
<b>Yellow</b>	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.
<b>Red</b>	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.

FN State Plan Evaluation Process – Planning and Identifying Work Groups	FN State Plan Evaluation Process – Planning and Identifying Work Groups
---	---

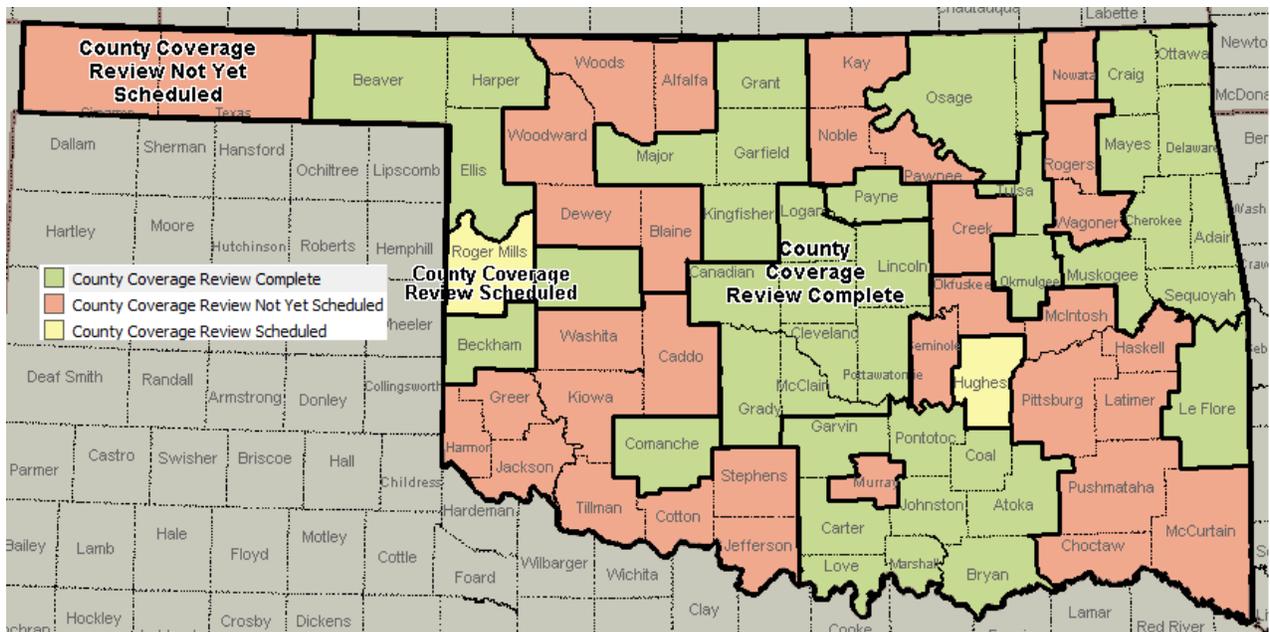

<b>Status on 21 March 2016</b>	<b>Prior Status</b>	<b>Green</b>	<b>Current Status</b>	<b>Green</b>
<b>Green</b>	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.			
<b>Yellow</b>	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.			
<b>Red</b>	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.			

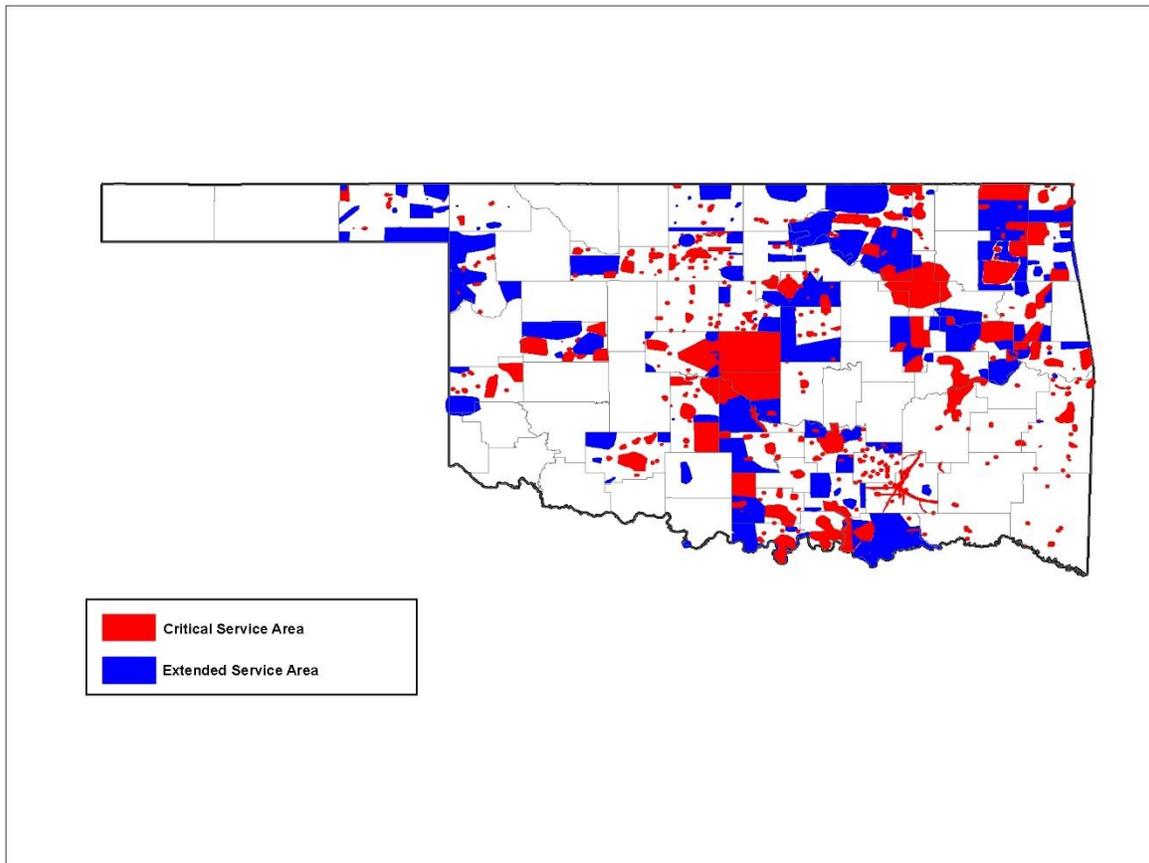

**Coverage Review Status**


The map above depicts the counties which have and have not been scheduled as well as those who have completed.

- Ian to assist David in completing coverage review for faster results
- 40 County Coverage Reviews held
- 2 County Coverage Reviews Scheduled
- 8 Tribal Coverage Reviews Complete: Chickasaw, Osage, Choctaw, Otoe-Missouria, Kickapoo, Iowa, Wyandotte and Tonkawa

State of Oklahoma State and Local Implementation Grant Program

Status on 21 March 2016	Prior Status	Green	Current Status	Green
Green	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.			
Yellow	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.			
Red	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.			

- Tribal Coverage Review Request Email Sent, 11/17
- Tribal Phone Calls made 1/22

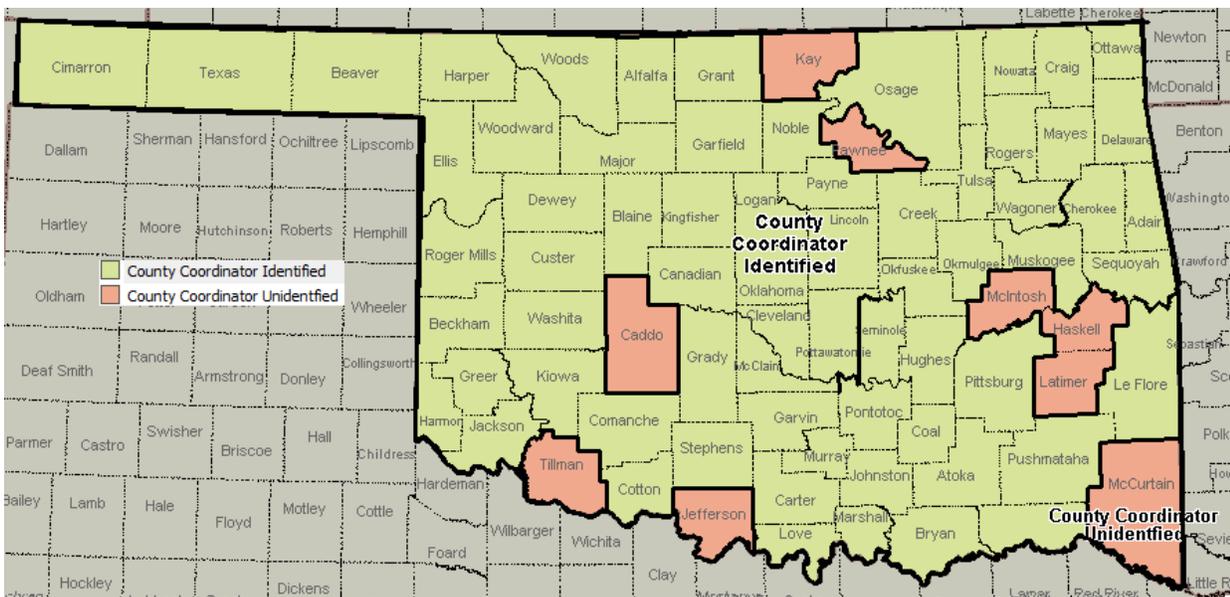

**Updated: County Coordinator**

This map depicts the Public Safety Entities (PSEs) from each county that have provided a county coordinator contact.

- County coordinator strategy: Emergency Manager, PSAP Manager, then Sheriff
  - County coordinator request emails sent 5/11
  - 69 county coordinators have been identified
  - 11 county coordinators have provided an updated contact list for their county
  - 10 tribal coordinators have been identified



State of Oklahoma State and Local Implementation Grant Program

Status on 21 March 2016	Prior Status	Green	Current Status	Green
<b>Green</b>	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.			
<b>Yellow</b>	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.			
<b>Red</b>	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.			
<p><b>UPDATE: Personnel Counts</b></p> <p>This map depicts the number of Public Safety Entities (PSEs) from each county that have provided personnel and vehicle counts.</p> <ul style="list-style-type: none"> <li>○ Strategy for accelerated data gathering Completed for FirstNet Data Collection Elements <ul style="list-style-type: none"> <li>▪ 46 Counties have provided personnel and vehicle counts for 100% of their agencies</li> <li>▪ 1110 agencies with personnel and vehicle counts</li> </ul> </li> <li>○ <b>Task 4 – Education and Outreach:</b> <ul style="list-style-type: none"> <li>○ Emergency Service Association Identification and Registration</li> <li>○ Preparation for second round of Outreach and Education meetings</li> <li>○ Update on Outreach Meetings conducted. <ul style="list-style-type: none"> <li>▪ Upcoming Association meetings <ul style="list-style-type: none"> <li>• Juana to Register</li> </ul> </li> </ul> </li> <li>○ Web Site edits in progress</li> </ul> </li> </ul>				

Status on 21 March 2016	Prior Status	Green	Current Status	Green
Green	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.			
Yellow	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.			
Red	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.			
<ul style="list-style-type: none"> <li>○ <b>Task 2 – Governance :</b> <ul style="list-style-type: none"> <li>○ Governance Interview Status:                             <ul style="list-style-type: none"> <li>● 4 Interviews Scheduled</li> <li>● 0 Interviews Complete</li> </ul> </li> <li>○ Governance document review and recommendations have been provided to governing board at January 21<sup>st</sup> quarterly meeting Possible issues- tribal representation of tribes on board, representation of local jurisdictions adequate, representation of regions adequate, limitations on use of onenet, can FirstNet commercial partner use onenet.</li> </ul> </li> <li>○ <b>Task 3 Tribal Participation</b> <ul style="list-style-type: none"> <li>○ Follow up with FN tribal team, assign action items.</li> <li>○ Tribal Webinar Conducted 6/25 by David Fein</li> <li>○ Tribal Leadership Letter Status</li> <li>○ Tribal Liaison meeting 5/12 on site meeting rescheduled for 7/2.</li> <li>○ ODOT Tribal Liaison contacted</li> <li>○ Tribes contact by Ian January 25<sup>th</sup>. 6 coordinators identified and 2 coverage reviews scheduled.</li> </ul> </li> <li>○ <b>Action Items</b></li> </ul>				
<h2 style="margin: 0;">Oklahoma PSBN Project Weekly Status Call Action Item Register</h2>				

State of Oklahoma State and Local Implementation Grant Program

Status on 21 March 2016	Prior Status	Green	Current Status	Green	
<b>Green</b>	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.				
<b>Yellow</b>	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.				
<b>Red</b>	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.				
Action Item	Owner	Date Assigned	Due Date	Priority (H, M, L)	Comments
Coverage Review Scheduling Assistance	Captain Baisden	12/28/2015	As needed	H	Phone calls for select counties
Association and Conference Calendar	Ian and Juana	11/30/2015	Updated Periodically	H	
Statewide Agencies to Include in coverage reviews and userpop	OKPSBN Team	8/3/2015	8/3/2015	H	
Completed Action Items					
ODOT Public Works 8 field divisions Personnel/Vehicle Counts	Ralph	11/30/2015	12/30/2015	H	Completed
LMR coverage GIS files	Nick	6/29/2015	7/13/2015	H	
Homeland Security Regional Coordinators	Ian	8/24/2015	8/27/2015	H	Will Schedule Coverage Reviews
Governance Draft Document	David Fein/ Rick	8/24/2015	8/27/2015	H	Review and Provide OKPSBN

State of Oklahoma State and Local Implementation Grant Program

Status on 21 March 2016	Prior Status	Green	Current Status	Green	
<b>Green</b>	The project is within 20% variance of the currently approved baseline for budget and schedule, and is expected to substantially meet all of the business objectives established in the startup report.				
<b>Yellow</b>	The project has exceeded 20% variance of the currently approved baseline for budget and/or schedule and is expected to substantially meet all of the business objectives established in the startup report.				
<b>Red</b>	The project is at risk of termination, or at risk of not substantially meeting the business objectives established in the startup report.				
<b>Homeland Security Regional Coordinators</b>	Nikki	8/24/2015	8/27/2015	H	Complete
<b>Oklahoma Email Blast</b>	Juana Riley	8/24/2015	8/24/2015	H	Complete
<b>Governance Draft Document</b>	Mathew Plache	8/24/2015	8/27/2015	H	Complete
<b>Critical Infrastructure</b>	Ben G/ Personnel	6/22/2015	7/13/2015	H	
<b>OKC and Tulsa outreach and education meetings letters sent and date set</b>	OKPSBN Team	6/22/2015	7/13/2015	H	Official Dates Set?
<b>Statewide incident data</b>	Ben G/ Personnel	6/22/2015	7/13/2015	H	

- **Invoices and Deliverables**
  - Work Approval Form outstanding
  
- **Upcoming Events, Travel, New Business:**
  - Osage Nation Tribal Meeting Completed 1/27/16
  - Citizens Pottawatomie Nation Tribal Coalition TBD
